Ysgol Y Deri Expansion
Construction Programme - Rev L

Line	Name	Duration (Working Weeks)	Start	Finish
	Construction Programme (1 WEEK EARLY WORKS + 60 WEEKS MAIN WORKS)	**69w 1d**	**13 Feb 23**	**05 Jul 24**
2	Early Works	1w	13 Feb 23	17 Feb 23
3	Roadworks	33w 4d	15 May 23	22 Jan 24
4	Lavernock Road Site Entrance	3w 2d	15 May 23	07 Jun 23
5	Fort Road Widening	18w 1d	04 Sep 23	22 Jan 24
6	Site Setup	8w 1d	22 May 23	18 Jul 23
7	Construction of New School	54w 4d	30 May 23	05 Jul 24
8	Substructure	18w 4d	30 May 23	09/10/23
9	Site Strip	3w	30 May 23	19 Jun 23
10	Pad Foundations	5w 2d	19 Jun 23	25 Jul 23
11	Ground Floor Slab	6w	29 Aug 23	09 Oct 23
12	Superstructure	12w	24 Jul 23	16/10/23
13	Steel Frame	5w	24 Jul 23	25 Aug 23
14	Metal Decking	2w 2d	21 Aug 23	06 Sep 23
15	Concrete on Metal Decking	2w	30 Aug 23	12 Sep 23
16	Fire Protection	4w	19 Sep 23	16 Oct 23
17	Envelope	18w 1d	12 Sep 23	30/01/24
18	Roof	13w	12 Sep 23	11/12/23
19	Elevations	16w 1d	26 Sep 23	30/01/24
20	North Elevation	16w 1d	26 Sep 23	30 Jan 24
21	East Elevation	10w 2d	09 Oct 23	19 Dec 23
22	South Elevation	13w 3d	13 Oct 23	30 Jan 24
23	West Elevation	10w 3d	03 Nov 23	30 Jan 24
24	Weathertight / Watertight	4w 1d	06 Nov 23	05 Dec 23
25	Internal Fitout	24w	31 Oct 23	01 May 24
26	Ground Floor	21w 2d	06 Nov 23	18 Apr 24
27	Pre Watertight	5w	06 Nov 23	08 Dec 23
28	Watertight	18w 1d	28 Nov 23	18 Apr 24
29	First Floor	21w 1d	20 Nov 23	01 May 24
30	Pre Watertight	5w	20 Nov 23	22 Dec 23
31	Watertight	18w 1d	11 Dec 23	01 May 24
32	Communal Areas	5w 4d	14 Mar 24	25 Apr 24
33	Plant Rooms	18w	31 Oct 23	18 Mar 24
34	Commissioning	22w	05 Dec 23	23 May 24
35	Utilities	24w 4d	27 Jun 23	18 Dec 23
36	Off Site	21w 4d	27 Jun 23	27 Nov 23
37	On Site	14w 4d	06 Sep 23	18 Dec 23
38	External Works	51w 4d	20 Jun 23	05/07/24

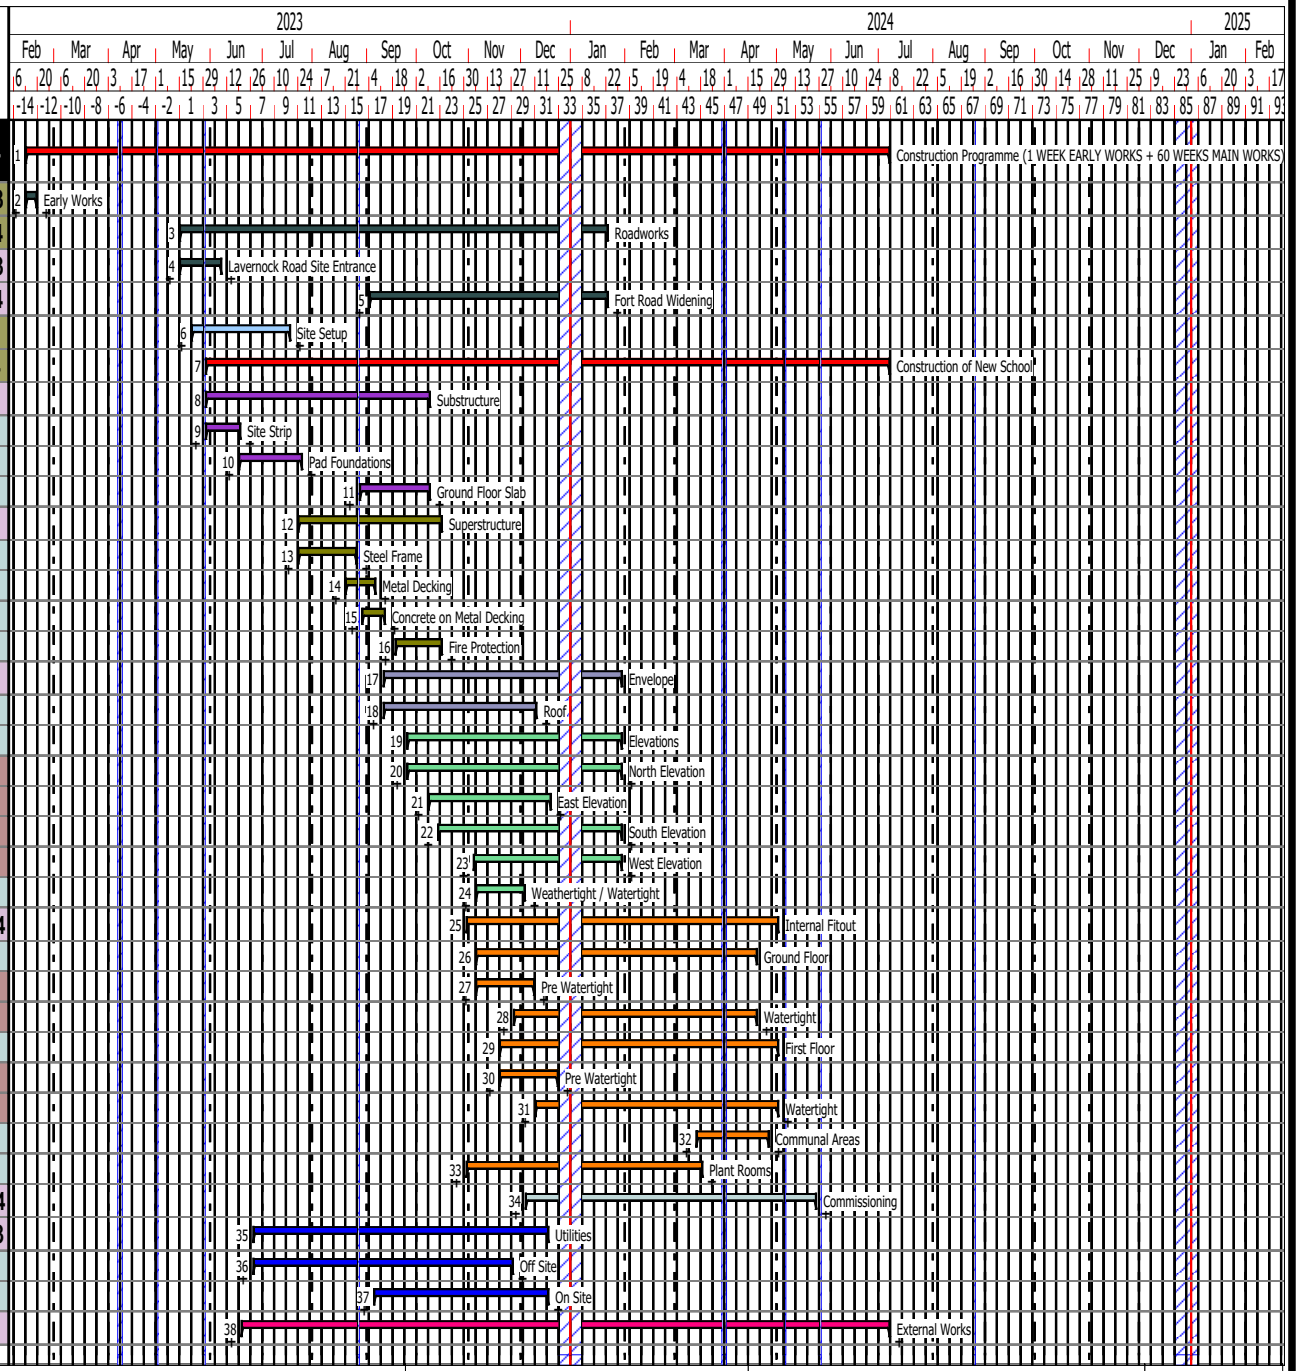

General Comment :	Author : ISG	Programme No: YYDE/CON/1
Rev. Comment : L	First Issued : 19/01/2023	Page 1 of 1

Revision: L
